Tollaust Pty Ltd - Lane Cove Tunnel

Marden St and Sirius Rd Stack Air Quality Monitoring Validated Data Report

01 August 2026 to 31 August 2026

Ref: DR.202608.LCT
Issue Date: 11/09/2026
Report prepared by: Tim Allfrey

Document Control

Revision	Date	Details	Prepared By	Approved By
0	11/09/2026	Original	TA	BN

Distribution


Format	Recipient	Details
PDF	Olivia Kieser	Olivia.Kieser@downergroup.com

Prepared by



Tim Allfrey
11 September 2026

Approved by



Bruno Nourdine
11 September 2026

Norditech Accreditations

We operate a fully compliant NATA-approved lab, and our engineers are factory-trained in the repair and maintenance of most types of gas analysers on the market, including circuit board level repairs. Our instrument technicians' training is constantly updated to stay current with the latest gas analyser market trends.

Certified System Quality ISO 9001 SAI GLOBAL
Certified System Environment ISO 14001 SAI GLOBAL
Certified System OHS ISO 45001 SAI GLOBAL

Accreditation number: 19660

NATA WORLD RECOGNISED ACCREDITATION

Table of Contents

Document Control **2**
Distribution **2**
Norditech Accreditations **2**
Table of Contents **3**
Figures **5**
Tables **5**
1. Executive Summary **7**
1.1 Compliance to limits 7
2. Introduction **7**
2.1 Project Background 7
2.2 Outlet Monitor Locations 8
2.3 Scope 8
3. Monitoring Equipment **9**
3.1 Outlet Monitors 9
4. Air Quality Limits **11**
5. Data Validation and Reporting **11**
5.1 Validation 11
5.2 Reporting 12
5.3 Data Collection 13
5.3.1 Data Availability 13
5.3.2 Unit Conversions 13
5.3.3 Combined Sirius Road South and Sirius Road North results 13
5.3.4 Accumulative Load 14
6. Calibrations and Maintenance **15**
6.1 Maintenance 15
6.2 Calibration 15
7. Above Goal Readings **17**
8. Documentation **18**
9. Results **19**
9.1 Data Availability 19
9.2 Tabulated Results 19

9.2.1 Summary of 30 minute Average Ventilation Outlet Data 19
9.2.2 Summary of 30 minute Average Flow, Relative Humidity and Temperature 20
9.2.3 Summary of Accumulated Load for Combined Stacks 21
9.3 Graphical Representations 22
9.3.1 Marden St Stack - Monthly Charts 22
9.3.1.1 Marden St Monthly CO Averages 22
9.3.1.2 Marden St Monthly VOC Averages 23
9.3.1.3 Marden St Monthly NO_x, NO_2 Averages 23
9.3.1.4 Marden St Monthly PM_{10} Averages 24
9.3.2 Sirius Rd Stack - Monthly Charts 25
9.3.2.1 Sirius Rd Monthly CO Averages 25
9.3.2.2 Sirius Rd Monthly VOC Averages 26
9.3.2.3 Sirius Rd Monthly NO_x, NO_2 Averages 26
9.3.2.4 Sirius Rd Monthly PM_{10} Averages 27
9.3.3 Accumulative Loads 28
9.3.3.1 Combined Stacks CO Accumulative Load 28
9.3.3.2 Combined Stacks VOC Accumulative Load 29
9.3.3.3 Combined Stacks NO_x Accumulative Load 29
9.3.3.4 Combined Stacks PM_{10} Accumulative Load 30
9.3.4 Marden St Stack - Three Monthly Trends 31
9.3.4.1 Marden St Three Monthly CO 1day Averages 31
9.3.4.2 Marden St Three Monthly VOC 1day Averages 32
9.3.4.3 Marden St Three Monthly NO_x, NO_2 1day Averages 32
9.3.4.4 Marden St Three Monthly PM_{10} 1day Averages 33
9.3.5 Sirius Rd Stack - Three Monthly Trends 34
9.3.5.1 Sirius Rd Three Monthly CO 1day Averages 34
9.3.5.2 Sirius Rd Three Monthly VOC 1day Averages 35
9.3.5.3 Sirius Rd Three Monthly NO_x, NO_2 1day Averages 35
9.3.5.4 Sirius Rd Three Monthly PM_{10} 1day Averages 36

10. Data Exceptions 37

11. Report Summary 39

12. Data validation explanations 40

Figures

Figure 1. Lane Cove Tunnel ventilation stack locations 8
Figure 2. Marden St CO Averages 22
Figure 3. Marden St VOC Averages 23
Figure 4. Marden St NOx, NO_2 Averages 23
Figure 5. Marden St PM_{10} Averages 24
Figure 6. Sirius Rd CO Averages 25
Figure 7. Sirius Rd VOC Averages 26
Figure 8. Sirius Rd NOx, NO_2 Averages 26
Figure 9. Sirius Rd PM_{10} Averages 27
Figure 10. Combined Stacks CO Accumulative Load 28
Figure 11. Combined Stacks VOC Accumulative Load 29
Figure 12. Combined Stacks NO_x Accumulative Load 29
Figure 13. Combined Stacks NO_x Accumulative Load 30
Figure 14. Marden St Three Monthly CO 1day Averages 31
Figure 15. Marden St Three Monthly VOC 1day Averages 32
Figure 16. Marden St Three Monthly NO_x, NO_2 1day Averages 32
Figure 17. Marden St Three Monthly PM_{10} 1day Averages 33
Figure 18. Sirius Rd Three Monthly CO 1day Averages 34
Figure 19. Sirius Rd Three Monthly VOC 1day Averages 35
Figure 20. Sirius Rd Three Monthly NO_x, NO_2 1day Averages 35
Figure 21. Sirius Rd Three Monthly PM_{10} 1day Averages 36

Tables

Table 1. Lane Cove Tunnel ventilation stack GPS Coordinates 8
Table 2. Monitoring requirements 9
Table 3. Outlet Measured Parameters and Instruments 10
Table 4. Ventilation Outlet Air Quality Limits 11
Table 5: Sirius Rd Reporting Condition criteria 14
Table 6. Indicative Maintenance requirements 15
Table 7. Daily Calibration Checks Times 15
Table 8. Marden St Last Scheduled Maintenance and Calibration Dates 16
Table 9. Sirius Rd South Last Scheduled Maintenance and Calibration Dates 16
Table 10. Sirius Rd North Last Scheduled Maintenance and Calibration Dates 17
Table 11. Marden St Above Goal Readings 17
Table 12. Sirius Rd Above Goal Readings 18
Table 13. Combined Stacks Annual Above Goal Readings 18
Table 14. LCT data availability 19
Table 15. Summary of 30-minute average data Marden St 19

Table 16. Summary of 30-minute average data Sirius Rd 20
Table 17. Summary of 30-minute average data Sirius Rd 20
Table 18. Summary of Accumulated Load for Combined Stacks 21
Table 19. Marden St Data Validation Table 37
Table 20. Sirius Rd South Data Validation Table 38
Table 21. Sirius Rd North Data Validation Table 39

Glossary

The following terms and abbreviations are used in this report

Abbreviation	Meaning
°C	Degrees Celsius
%	Percent
CO	Carbon monoxide
eq.	Equivalents
kPa	kiloPascal
mg/m^3	Milligrams per cubic meter at dry, standard temperature and pressure (0°C and 101.3 kPa)
NMHC	Non-methane hydrocarbons
NO	Nitric oxide
NO_2	Nitrogen dioxide
NO_x	Oxides of nitrogen
RH	Relative Humidity
TSP	Total Suspended Particulate
VOC	Volatile organic compounds
VSO	Ventilation Stack Outlet

1. Executive Summary

The Lane Cove Tunnel runs for 3.6km between North Ryde and Artarmon, linking the M2 Motorway and the Gore Hill Freeway and forms part of Sydney's motorway network. The tunnel commenced operation in March 2007.

Two stacks provide ventilation for the tunnel, one at the western end of the tunnel (Sirius Road, Lane Cove West), and one at the eastern end of the tunnel (Marden St, Artarmon). The Sirius Road stack comprises two partitions, north and south. Sirius Road results are a combined weighted average to the two partitions.

This report presents the monthly validated stack data for August 2026 to Tollaust Pty Ltd for the Lane Cove Tunnel.

1.1 Compliance to limits

The Minister's Conditions of Approval (MCoA) designates limits to which pollutants being discharged from the ventilation stacks must meet. (MCoA 173).

There were nil exceedances of the prescribed limits during the reporting period.

2. Introduction

2.1 Project Background

Norditech were contracted by Tollaust Pty Ltd in December 2018 to provide continuous stack air quality monitoring and reporting services for Lane Cove Tunnel.

Norditech is a NATA accredited organisation (Accreditation Number 19660)

Addresses of relevant parties:

Norditech Pty Ltd
2/87 Station Rd
Seven Hills NSW 2147

Downer Pty Ltd
610 Pennant Hills Rd
West Pennant Hills, NSW 2125

This report presents the validated Marden St and Sirius Rd ventilation stack data for August 2026.

- Describe air quality measurements.
- Reports any readings above the LCT Limits.
- Compare monitoring results.
- It has been quality assured.

2.2 Outlet Monitor Locations

The locations of the Marden St and Sirius Rd ventilation stacks are detailed in the table and figure below.

Location	Latitude	Longitude
Marden St (Eastern Stack)	-33.815025°	151.179246°
Sirius Rd (Western Stack)	-33.807887°	151.146074°

Table 1. Lane Cove Tunnel ventilation stack GPS Coordinates

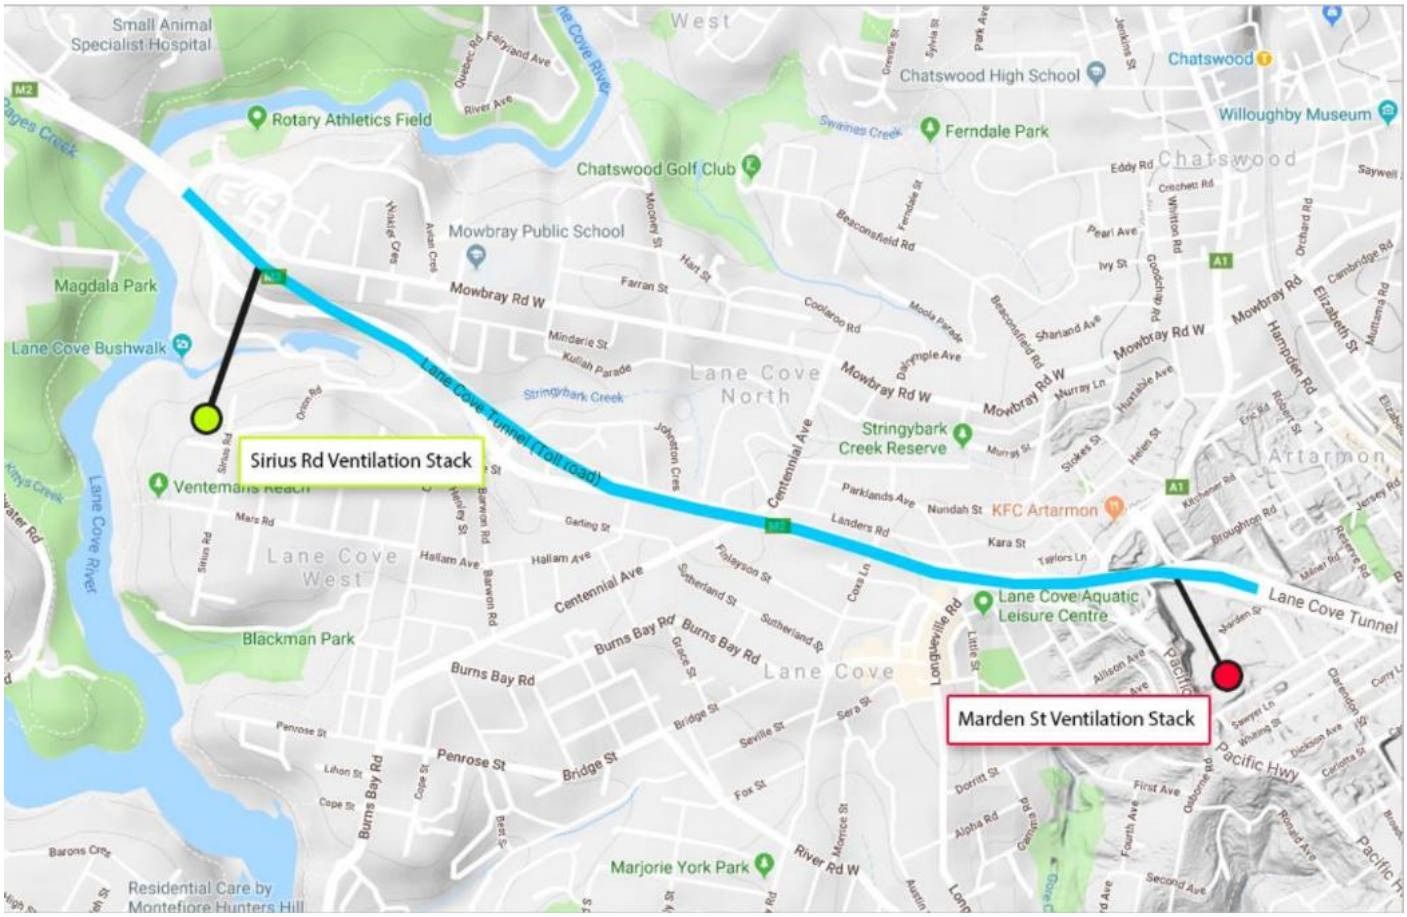


Figure 1. Lane Cove Tunnel ventilation stack locations

2.3 Scope

In tunnel air is discharged via two ventilation stacks – one located at Marden St, Artarmon, and one located at Sirius Rd, Lane Cove West. The Sirius Rd stack comprises of two separate partitions (North and South). For each stack, monitoring as per the requirements of MCoA 172 is undertaken. Each partition of the Sirius Rd stack is monitored by separate air quality monitoring stations.

Gaseous parameters are sampled by an extractive sampling system with automatic purging. Volatile organic compounds are measured using the flame ionization detection principle. Oxides of nitrogen are measured using chemiluminescence. Carbon monoxide is measured using non-dispersive infra-red absorption.

Particulates PM10 and PM2.5 are measured using tapered element oscillating microbalances, via an isokinetic sampling system.

Monthly routine maintenance is undertaken by Norditech. Maintenance is performed as per the relevant Australian Standard or in house method. Maintenance cycles generally involve 1, 3, 6 and 12 monthly scheduled items.

3. Monitoring Equipment

3.1 Outlet Monitors

The Instrument of Approval requires each ventilation outlet to be continuously monitored in accordance with the requirements of Table 2.

Pollutant / Parameter	Frequency	Equivalent Reference Method	Description of the Method
CO	Continuous	In house method TP.003	In-house methods 9.5 - Extractive dilution and 6.3 - Carbon monoxide by gas filter correlation spectrophotometry
NO, NOx, NO2	Continuous	In house method TP.001	In-house methods 9.5 – Extractive dilution and 6.1 - Oxides of nitrogen by chemiluminescence
PM_{10}	Continuous	AS/NZS 3580.9.8	In-house method 7.5 – Measurement of PM10, PM2.5 and TSP using Beta Attenuation Monitor.
		In house method TP.005	
		AS 4323.1	
$PM_{2.5}$	Continuous	In house method TP.026	In-house method 7.5 – Measurement of PM10, PM2.5 and TSP using Beta Attenuation Monitor.
		AS 4323.1	
CH4, NMHC, VOC[2]	Continuous	In house method TP.006	In-house method 9.5 - Monitoring of methane and non-methane hydrocarbons by direct extraction
Relative Humidity	Continuous	In house method TP.014	In-house method 9.8 – Continuous monitoring of moisture using relative humidity and temperature probe
Temperature	Continuous	In house method TP.012	In-house method 9.3 - Temperature by instrumental techniques
Flow Rate	Continuous	TBA	In-house method 9.2 - Gas flow by ultrasonic techniques

Table 2. Monitoring requirements

The pollutant and parameters will be continuously measured using the instruments identified in Table 3 below.

Pollutant/ Parameter	Instrument	Units of Measure	Range	Resolution	Uncertainty
CO	Ecotech Serinus S30	mg/m^3	0 – 123 mg/m^3	0.01 $\mu g/m^3$	± 8.2% of reading at 62.5mg/m^3 (k=1.96)
NO	Ecotech Serinus S40	mg/m^3	0 – 31ppm	0.01ppb	± 8.1% of reading for range 25.7 – 32.8mg/m^3 (k=1.96)
NO_x	Ecotech Serinus S40	mg/m^3	0 – 33 ppm	0.01 ppb	± 8.1% of reading for range 25.7 – 32.8mg/m^3 (k=1.96)
NO_2	Ecotech Serinus S40	mg/m^3	0 – 33 ppm	0.01 ppb	± 8.5% of reading at 25.7mg/m^3 (k=1.96)
CH_4	Baseline 9000, ENVEA HC51M	mg/m^3	0 – 17ppm	0.1 ppm	±12% of reading + 0.3mg/m^3 for range 3.5 – 17mg/m3 (k=2.0)
NMHC (as propane)	Baseline 9000, ENVEA HC51M	mg/m^3	0 – 20 ppm	0.01 ppm	±13% of reading + 0.56mg/m^3 for range 3.5 – 20mg/m3 (k=2.0)
PM_{10}	Rupprecht & Patashnick TEOM with Ecotech and Norditech ISS isokinetic sampling system	$\mu g/m^3$	0 – 5000 µg/m3	0.1 µg/m3	±5.0 µg/m3 or 3.6% of reading, whichever is the greater (k=1.96)
PM_{25}	Rupprecht & Patashnick TEOM with Ecotech and Norditech ISS isokinetic sampling system	$\mu g/m^3$	0 – 5000 µg/m3	0.1 µg/m3	±5.0 µg/m3 or 3.6% of reading, whichever is the greater (k=1.96)
Temperature	Vaisala HMT330	°C	0 - 50 °C	0.1 °C	± 0.6 ˚C, (k=2.0)
Relative Humidity	Vaisala HMT330	%	0 - 100 %	1 %	± 6%, (k=2.0)
Flow Rate	Flowsic100 USD 55SSTI Ultrasonic flow sensor	m^3/s	±40 m^3/s	1 m^3/s	±0.1 for velocity measurement1

Table 3. Outlet Measured Parameters and Instruments

4. Air Quality Limits

Air quality goals provided are provided in Condition 173 of the Minister's Conditions of Approval issued by the Director-General for the Lane Cove Tunnel project. The air quality goals are shown in the table below.

Location	Pollutant / Parameter	Type of Measurement	Concentration Limit	Unit
Marden St (Eastern Stack)	CO	Average – 30 minutes	62.5	mg/m^3
	NO_x	Average – 30 minutes	25.7	mg/m^3
	PM_{10}	Average – 30 minutes	1200	$\mu g/m^3$
	VOC (as propane)	Average – 30 minutes	6.3	mg/m^3
Sirius Rd (Western Stack)	CO	Average – 30 minutes	62.5	mg/m^3
	NO_x	Average – 30 minutes	32.8	mg/m^3
	PM_{10}	Average – 30 minutes	1600	$\mu g/m^3$
	VOC	Average – 30 minutes	6.3	mg/m^3
Combined Stacks	CO	Annual	1530	t/annum
	NO_x	Annual	229	t/annum
	PM10	Annual	14	t/annum
	VOC	Annual	153	t/annum

Table 4. Ventilation Outlet Air Quality Limits

5. Data Validation and Reporting

5.1 Validation

Data validation is performed as per Norditech's data validation procedure TP.022. The data validation process identifies any data that is deemed not to be valid. This data is flagged as invalid in the database and is removed from the reported data.

Data may be deemed invalid for several reasons, including but not limited to:

- Instrument fault
- Instrument calibration out of tolerance
- Maintenance activities

For further details and explanations of reasons for invalidating data, please refer to section Data Validation Explanations.

Initial visual inspection of data is performed by inspection of graphs to identify any anomalies in the data set.

Site visit logs and maintenance and calibration certificates are cross referenced to the data set and any data affected by maintenance activities are flagged.

Instrument drift and calibration tolerances are checked and data flagged in the database as necessary as per NATA compliance requirements.

5.2 Reporting

The data is reported in real time at the Lane Cove Tunnel website (URL. http://lanecovetunnel.com/))

Summary monthly data is recorded and reported within the OMCS and is included in the attachments to this report.

a. Carbon Monoxide
b. Oxides of Nitrogen
c. Nitrogen Dioxide
d. Nitrogen Monoxide
e. Volatile Organic Compounds
f. PM_{10}
g. $PM_{2.5}$
h. Stack Temperature
i. Stack Flow
j. Relative Humidity

Averages are based on all readings within the averaging period.

In addition to this, the OMCS can generate ad hoc reports for specific events or periods, and these will be included in the report as required, to provide additional detail for an abnormal event or incident.

Data reported via the OMCS has not been validated. This report provides validated data for the VSO sensors.

All data within this report is reported as 'End Time'. Ie the 1hour average result for 2:00 is the average of the 1minute data from 1:00 through to 2:00.

5.3 Data Collection

At each Air Quality Monitoring Station, data is logged to a Congrego data logger at 5-minute average intervals. Each 5-minute average is calculated from data sampled at 10 second intervals.

Data is transferred automatically to Norditech's data collection software via a TCP/IP link, at a frequency of not greater than 1 hour. Two datasets are maintained by Norditech, one for data validation and reporting purposes, and a non-validated data set for reference purposes.

5.3.1 Data Availability

Data availability refers to the amount of available data for the reporting period. Data availability is calculated using the following formula:

$$\text{Data availability } \% = \frac{\text{sum of available data points}}{\text{sum of possible data points}} * 100$$

Where:

- Sum of available data points is the number of validated 1 hour average data points for the reporting period
- Sum of possible data points is the number of theoretically available data points for the reporting period

5.3.2 Unit Conversions

Total oxides of nitrogen (NOx) results are expressed as NO2 equivalents in mg/m3. As of 1/03/2021, VOC results are expressed as non-methane hydrocarbons as propane equivalents in mg/m3. Prior to this date VOC results were expressed as total VOCs as methane equivalent.

Stack velocity readings are converted to flow rate using the following stack areas:

- Marden Street Stack area 59.8919 m2
- Sirius Road Stack – North Partition area 35.95 m2
- Sirius Road Stack – South Partition area 36.19 m2

Pollutant and flow data are reported at reference conditions: 0°C, 101.325 kPa, dry.

5.3.3 Combined Sirius Road South and Sirius Road North results

Data from the Sirius Road stack are combined results of the north and south partitions. Stack velocity is used to determine whether a partition is active or inactive, and this determines the calculation for the total Sirius Road ventilation stack results.

The table below shows the criteria used to determine how the total Sirius Road ventilation stack data is calculated.

LCT Tunnel Sirius Rd Ventilation Stack Reporting Conditions	
Partitions Active	Calculation
None	Combined result is based on weighted total from both partitions. Weighting is calculated as a function of the ratio of partition flows to total flow
One	Active partition is reported
Both	Combined result is based on weighted total from both partitions. Weighting is calculated as a function of the ratio of partition flows to total flow
Unknown in either partition	No result provided as it cannot be determined whether each partition is active or not

Table 5: Sirius Rd Reporting Condition criteria

5.3.4 Accumulative Load

Accumulative loads are calculated from the monthly measured emission in tonnes for each stack for CO, NOx, PM10 and VOC. The measured emissions are converted to an estimated monthly total emission by taking into account the data capture of each parameter, using the following formula:

$$estimated\ monthly\ total\ emission = \frac{measured\ monthly\ emission}{available\ data\ \%} * 10$$

The estimated monthly total emissions for each parameter for each stack are then added together to give the total emission per parameter per month.

The accumulative load is then calculated as the sum of the previous 12 months estimated total emission for each parameter.

If there is less than 50% data availability for any parameter, then data for the last valid previous month (i.e. above 50% data availability) is substituted.

6. Calibrations and Maintenance

6.1 Maintenance

Device	Frequency
Outlet Air Quality Sensors – CEMS Gas monitors	1 monthly
Outlet Air Quality Sensors – CEMS Particulate Monitor	1 monthly
Outlet Air Quality Sensors – CEMS Meteorological Sensors	6 monthly
Outlet Air Quality Sensors – CEMS Velocity Sensors	Based on the Manual Stack Testing frequency

Table 6. Indicative Maintenance requirements

6.2 Calibration

The table below identifies the times at which the daily gaseous parameter automatic span and zero checks are performed.

Further to the span and zero checks, the CO analysers perform nightly background reference cycles.

This data is removed from the dataset, however are not included in the data validation tables.

Nightly span and zero times for NO, NO_2, NO_x, CO, CH4 and NMHC			
Station	**Parameters**	**Span / Zero cycle time**	**Daily Calibration Checks Times**
Marden St	CO	1:00 – 2:00	23:45 – 23:50
	NO, NO2, NOx	1:00 – 2:00	-
	VOC	1:00 – 2:00	-
Sirius Rd South	CO	1:00 – 2:00	23:45 – 23:50
	NO, NO2, NOx	1:00 – 2:00	-
	VOC	1:00 – 2:00	-
Sirius Rd North	CO	1:00 – 2:00	23:45 – 23:50
	NO, NO2, NOx	1:00 – 2:00	-
	VOC	1:00 – 2:00	-

Table 7. Daily Calibration Checks Times

There are no valid data available for all gaseous parameters during these times. These automatic calibration cycles are not included in the data validation tables in Section 8.

The CEMS particulate monitors are to be manually calibrated at 3 monthly intervals as described in the Operation and Maintenance manuals prepared for the project. The CEMS particulate monitors will also undergo gravimetric correlation testing at yearly intervals as described in the Operation and Maintenance manuals prepared for the project.

A list of all the devices and the latest calibration details are included in the table below, and in an excel spreadsheet.

Lane Cove Tunnel Ventilation Stack Outlet Last Scheduled Calibration Dates – August 2026				
Marden St				
Sensor	**Date of Last Scheduled Maintenance**	**Maintenance Type**	**Date of Last Scheduled Calibration**	**Calibration Frequency**
CO	5/08/2026	12 Monthly	5/08/2026	1 Monthly
$NO/NO_2/No_x$	5/08/2026	12 Monthly	5/08/2026	1 Monthly
VOC	5/08/2026	12 Monthly	5/08/2026	1 Monthly
PM10	11/08/2026	12 Monthly	11/08/2026	1 Monthly
PM2.5	11/08/2026	12 Monthly	11/08/2026	1 Monthly
Temperature	11/08/2026	12 Monthly	11/08/2026	6 Monthly
Relative Humidity	11/08/2026	12 Monthly	11/08/2026	6 Monthly
Flow Rate	N/A	N/A	09/08/2024	Based on stack testing frequency

Table 8. Marden St Last Scheduled Maintenance and Calibration Dates

Lane Cove Tunnel Ventilation Stack Outlet Last Scheduled Calibration Dates – August 2026				
Sirius Rd South				
Sensor	**Date of Last Scheduled Maintenance**	**Maintenance Type**	**Date of Last Scheduled Calibration**	**Calibration Frequency**
CO	3/08/2026	1 Monthly	3/08/2026	1 Monthly
$NO/NO_2/No_x$	3/08/2026	1 Monthly	3/08/2026	1 Monthly
VOC	3/08/2026	1 Monthly	3/08/2026	1 Monthly
PM10	3/08/2026	1 Monthly	3/08/2026	1 Monthly
PM2.5	3/08/2026	1 Monthly	3/08/2026	1 Monthly
Temperature	13/07/2026	6 Monthly	13/07/2026	6 Monthly
Relative Humidity	13/07/2026	6 Monthly	13/07/2026	6 Monthly
Flow Rate	N/A	N/A	09/08/2024	Based on stack testing frequency

Table 9. Sirius Rd South Last Scheduled Maintenance and Calibration Dates

Lane Cove Tunnel Ventilation Stack Outlet Last Scheduled Calibration Dates – August 2026				
Sirius Rd North				
Sensor	**Date of Last Scheduled Maintenance**	**Maintenance Type**	**Date of Last Scheduled Calibration**	**Calibration Type**
CO	3/08/2026	6 Monthly	3/08/2026	1 Monthly
$NO/NO_2/No_x$	3/08/2026	6 Monthly	3/08/2026	1 Monthly
VOC	3/08/2026	6 Monthly	3/08/2026	1 Monthly
PM10	3/08/2026	6 Monthly	3/08/2026	1 Monthly
PM2.5	3/08/2026	6 Monthly	3/08/2026	1 Monthly
Temperature	5/08/2026	6 Monthly	5/08/2026	6 Monthly
Relative Humidity	5/08/2026	6 Monthly	5/08/2026	6 Monthly
Flow Rate	N/A	N/A	09/08/2024	Based on stack testing frequency

Table 10. Sirius Rd North Last Scheduled Maintenance and Calibration Dates

7. Above Goal Readings

Instances of the ventilation stack pollutants exceeding the MCoA goals during the reporting period are presented in the table below.

There were nil exceedances of the prescribed limits during the reporting period.

Lane Cove Tunnel – Marden St Above Goal Readings – August 2026						
Pollutant	**Concentration Limit**	**Units**	**Averaging Period**	**Number of Above Goal Readings**	**Date Time of Above Goal Reading**	**Above Goal Reading**
CO	62.5	mg/m^3	30 minutes	0	-	-
NO_x	25.7	mg/m^3	30 minutes	0	-	-
PM_{10}	1200	$\mu g/m^3$	30 minutes	0	-	-
VOC	6.3	mg/m^3	30 minutes	0	-	-

Table 11. Marden St Above Goal Readings

Lane Cove Tunnel – Sirius Rd Above Goal Readings – August 2026						
Pollutant	**Concentration Limit**	**Units**	**Averaging Period**	**Number of Above Goal Readings**	**Date Time of Above Goal Reading**	**Above Goal Reading**
CO	62.5	mg/m^3	30 minutes	0	-	-
NO_x	32.8	mg/m^3	30 minutes	0	-	-
PM_{10}	1600	$\mu g/m^3$	30 minutes	0	-	-
VOC	6.3	mg/m^3	30 minutes	0	-	-

Table 12. Sirius Rd Above Goal Readings

Lane Cove Tunnel – Combined Stacks Above Goal Readings – August 2026						
Pollutant	**Concentration Limit**	**Units**	**Averaging Period**	**Number of Above Goal Readings**	**Date Time of Above Goal Reading**	**Above Goal Reading**
CO	1530	t/annum	Annual	0	-	-
NO_x	229	t/annum	Annual	0	-	-
PM_{10}	14	t/annum	Annual	0	-	-
VOC	153	t/annum	Annual	0	-	-

Table 13. Combined Stacks Annual Above Goal Readings

8. Documentation

Validated data for Marden St Stack is presented in the Excel workbook named "202608 LCT Marden St Stack Validated data.xlsx". The workbook consists of the following sheets:

1. Cover
2. Marden St 5m Avg
3. Marden St Span Zero Data
4. Marden St Data Validation

Validated data for Sirius Rd Stack is presented in the Excel workbook named "202608 LCT Sirius Rd Stack Validated data.xlsx". The workbook consists of the following sheets:

1. Cover
2. Sirius Rd Combined 5m Avg
3. Flow Temp RH Individual 5m Avg
4. Sirius Rd South Span Zero Data
5. Sirius Rd North Span Zero Data
6. Sirius Rd South Data Validation
7. Sirius Rd North Data Validation

9. Results

9.1 Data Availability

Data availability for the ventilation stack outlet sensors is provided in the table below.

LCT Tunnel – Ventilation Stack Data Availability – August 2026								
Location	**CO (%)**	**NO (%)**	**NO2 (%)**	**NOx (%)**	**PM_{10} (%)**	**$PM_{2.5}$ (%)**	**VOC (%)**	**Flow (%)**
Marden St Stack	84.8%	88.8%	88.8%	88.8%	92.8%	93.4%	88.8%	93.9%
Sirius Rd Stack	93.2%	93.6%	93.6%	93.6%	97.6%	97.4%	92.2%	98.8%

Table 14. LCT data availability

9.2 Tabulated Results

9.2.1 Summary of 30 minute Average Ventilation Outlet Data

The following table presents 30 minute average minimum, maximum and daily average data for the Marden St Stack, and Sirius Rd combined stack.

30 minute averages are calculated from 5 minute average data. The daily average is calculated from 30 minute average data.

LCT Tunnel – Marden St Stack Summary – August 2026								
	CO	**NO**	**NO_2**	**NO_x**	**PM_{10}**	**$PM_{2.5}$**	**VOC**	**Flow**
	mg/m^3	mg/m^3	mg/m^3	mg/m^3	$\mu g/m^3$	$\mu g/m^3$	mg/m^3	m^3/s
	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average
Minimum	-0.12	0.02	0.04	0.07	-3.49	-9.72	-0.01	293.40
Maximum	4.81	3.17	0.63	5.50	193.03	109.48	0.42	579.63
Average	1.35	0.63	0.17	1.13	38.47	16.37	0.10	460.33
Limit	62.50	N/A	N/A	25.70	1200.00	N/A	6.30	N/A

Table 15. Summary of 30-minute average data Marden St

LCT Tunnel – Sirius Rd Stack Summary – August 2026								
	CO	**NO**	**NO_2**	**NO_x**	**PM_{10}**	**$PM_{2.5}$**	**VOC**	**Flow**
	mg/m^3	mg/m^3	mg/m^3	mg/m^3	$\mu g/m^3$	$\mu g/m^3$	mg/m^3	m^3/s
	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average
Minimum	0.03	-0.00	0.02	0.02	-2.54	-5.56	0.07	7.56
Maximum	1.88	0.92	0.37	1.66	108.28	86.70	1.87	426.22
Average	0.69	0.21	0.09	0.41	32.32	21.48	0.18	360.26
Limit	62.50	N/A	N/A	32.80	1600.00	N/A	6.30	N/A

Table 16. Summary of 30-minute average data Sirius Rd

9.2.2 Summary of 30 minute Average Flow, Relative Humidity and Temperature

The following table presents 30 minute average minimum, maximum and daily average flow, relative humidity, and temperature data for the Marden St Stack, and Sirius Rd North and South partitions.

30 minute averages are calculated from 5 minute average data. The daily average is calculated from 30 minute average data.

LCT Tunnel Ventilation Stack Flow, RH, Temperature Summary– August 2026									
Parameter	**Marden St (Eastern Stack)**			**Sirius Rd – South Partition**			**Sirius Rd – North Partition**		
	Flow	**RH**	**Temperature**	**Flow**	**RH**	**Temperature**	**Flow**	**RH**	**Temperature**
	m^3/s	%	°C	m^3/s	%	°C	m^3/s	%	°C
	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average	30 minute average
Minimum	293.40	29.41	15.19	3.96	33.81	8.44	7.56	20.57	13.88
Maximum	579.63	77.40	23.02	71.86	93.35	21.02	382.34	87.20	23.49
Average	460.33	53.19	19.43	10.13	67.83	14.45	360.28	47.47	19.51

Table 17. Summary of 30-minute average data Sirius Rd

9.2.3 Summary of Accumulated Load for Combined Stacks

Lane Cove Tunnel Ventilation Stack Outlet Accumulative Load September 2025 – August 2026				
Location	**Carbon Monoxide**	**Oxides of Nitrogen**	**PM_{10}**	**VOC**
	Tonnes	**Tonnes**	**Tonnes**	**Tonnes**
Accumulative Load for past 12 months	35.56	24.86	1.27	3.89
Annual Limit (Tonnes)	1530	229	14	153

Table 18. Summary of Accumulated Load for Combined Stacks

9.3 Graphical Representations

9.3.1 Marden St Stack - Monthly Charts

The following charts present 30-minute average minimum, maximum and daily average data CO, NOx, PM10 and VOC for the Marden St Stack.

30-minute averages are calculated from 5-minute average data. The daily average is calculated from 30-minute average data.

9.3.1.1 Marden St Monthly CO Averages

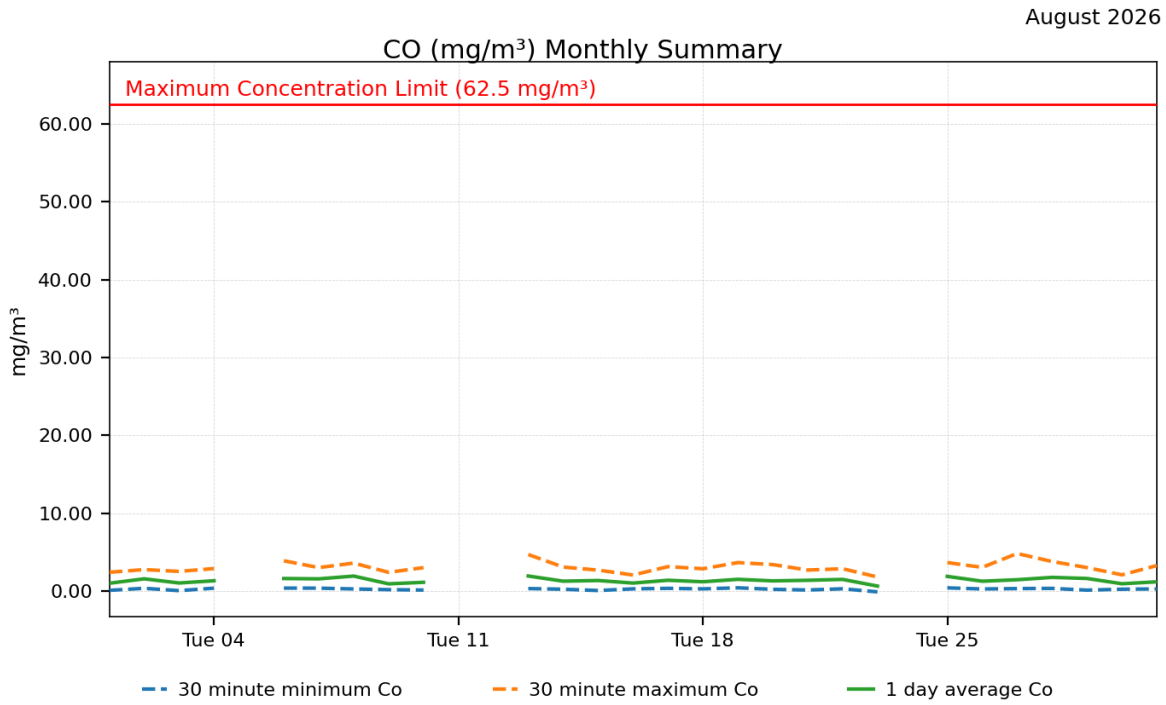


Figure 2. Marden St CO Averages

9.3.1.2 Marden St Monthly VOC Averages

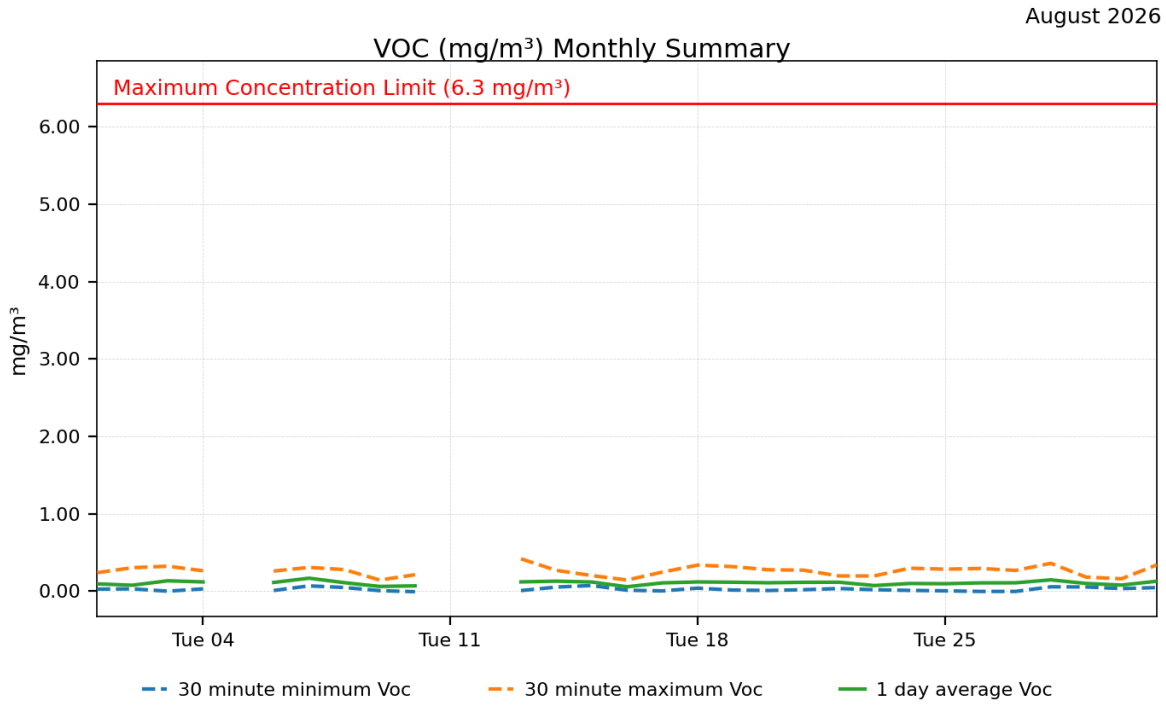


Figure 3. Marden St VOC Averages

9.3.1.3 Marden St Monthly NO_x, NO_2 Averages

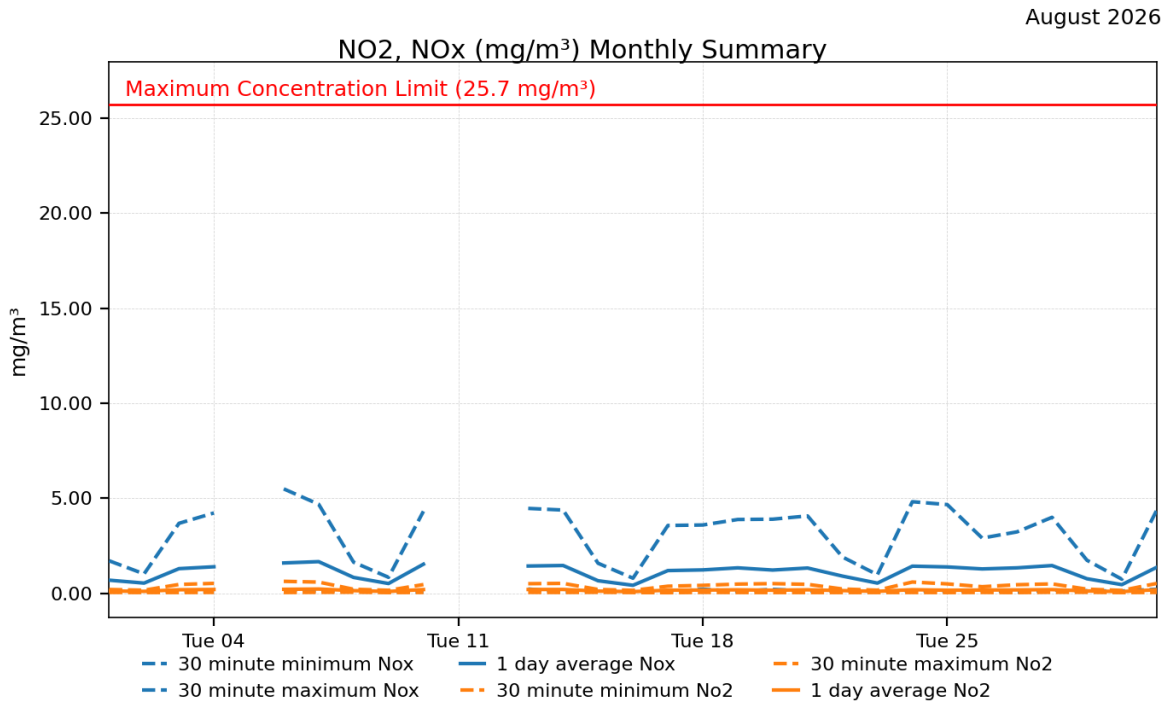


Figure 4. Marden St NOx, NO_2 Averages

9.3.1.4 Marden St Monthly PM_{10} Averages

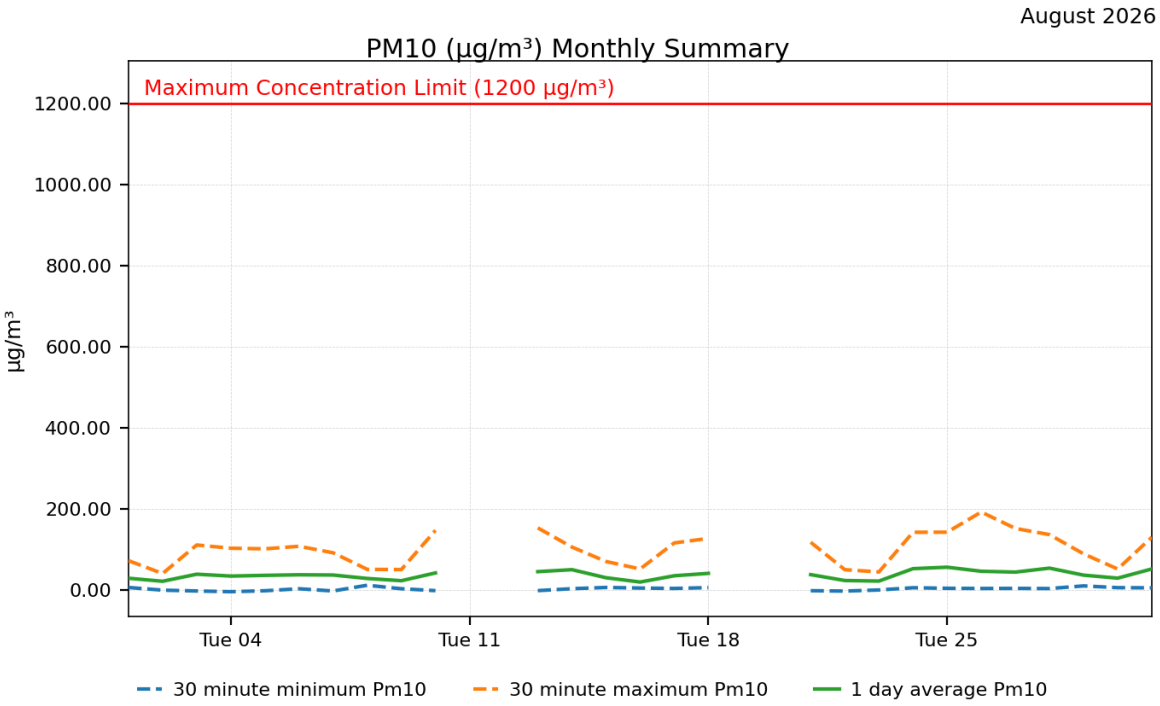


Figure 5. Marden St PM_{10} Averages

9.3.2 Sirius Rd Stack - Monthly Charts

The following charts present 30-minute average minimum, maximum and daily average data CO, NOx, PM10 and VOC for the Marden St Stack, and Sirius Rd combined stack.

30-minute averages are calculated from 5-minute average data. The daily average is calculated from 30-minute average data.

9.3.2.1 Sirius Rd Monthly CO Averages

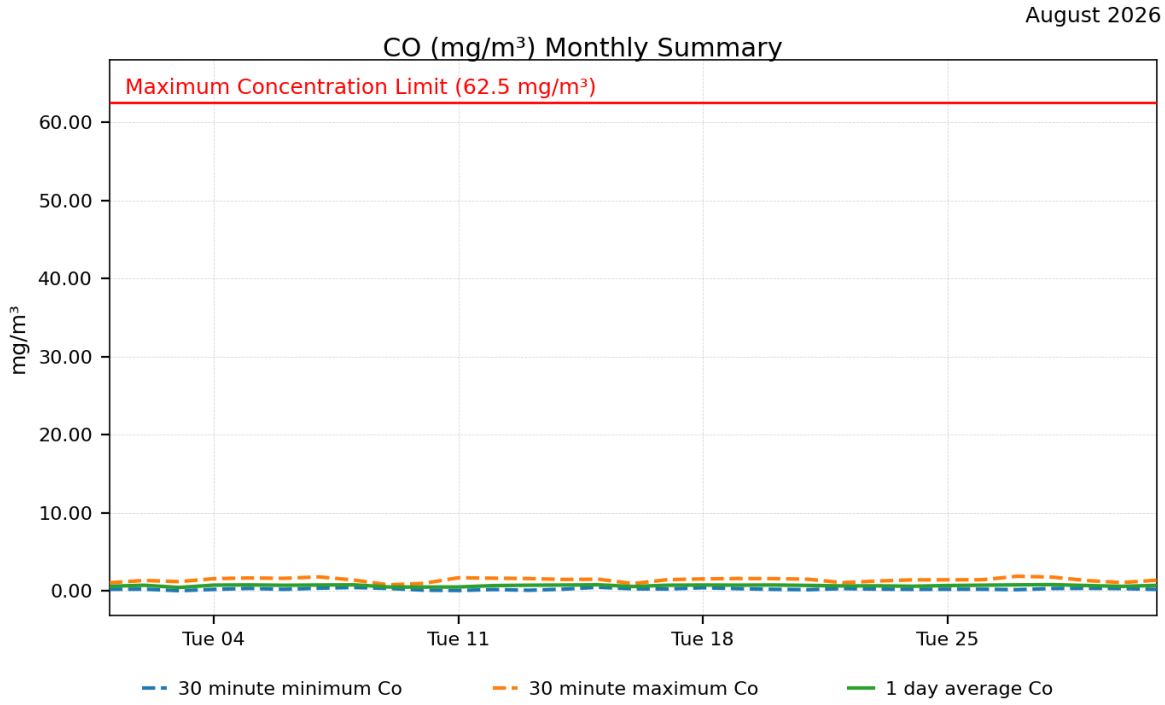


Figure 6. Sirius Rd CO Averages

9.3.2.2 Sirius Rd Monthly VOC Averages

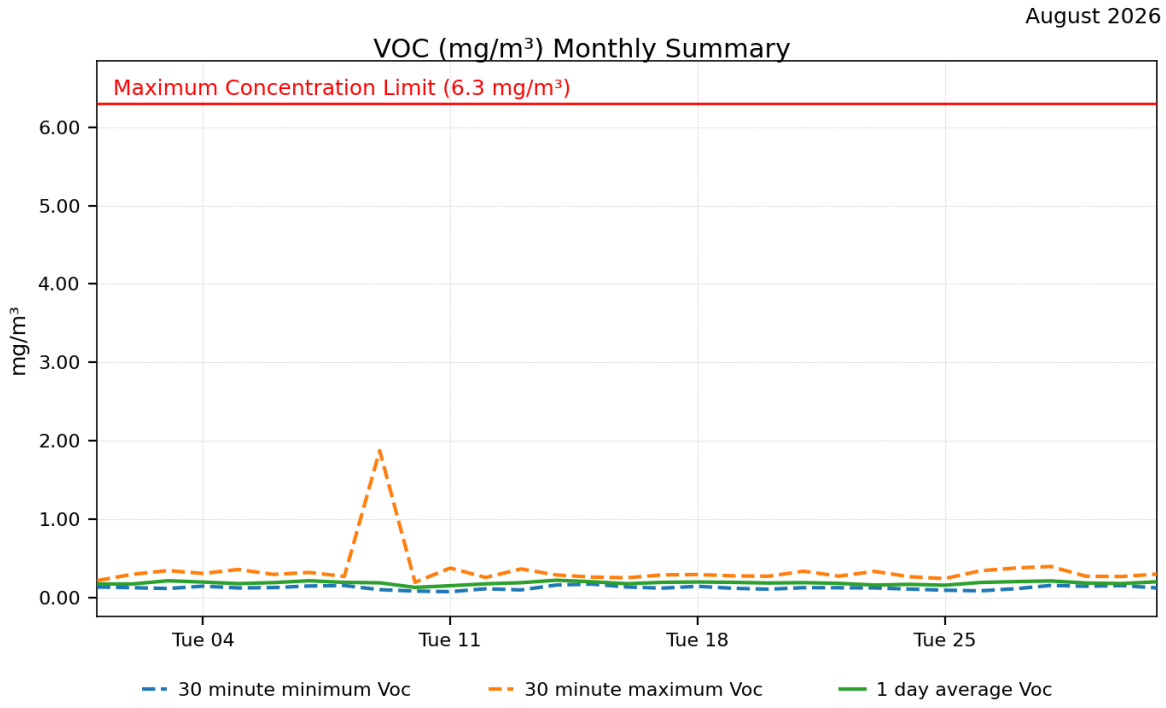


Figure 7. Sirius Rd VOC Averages

9.3.2.3 Sirius Rd Monthly NO_x, NO_2 Averages

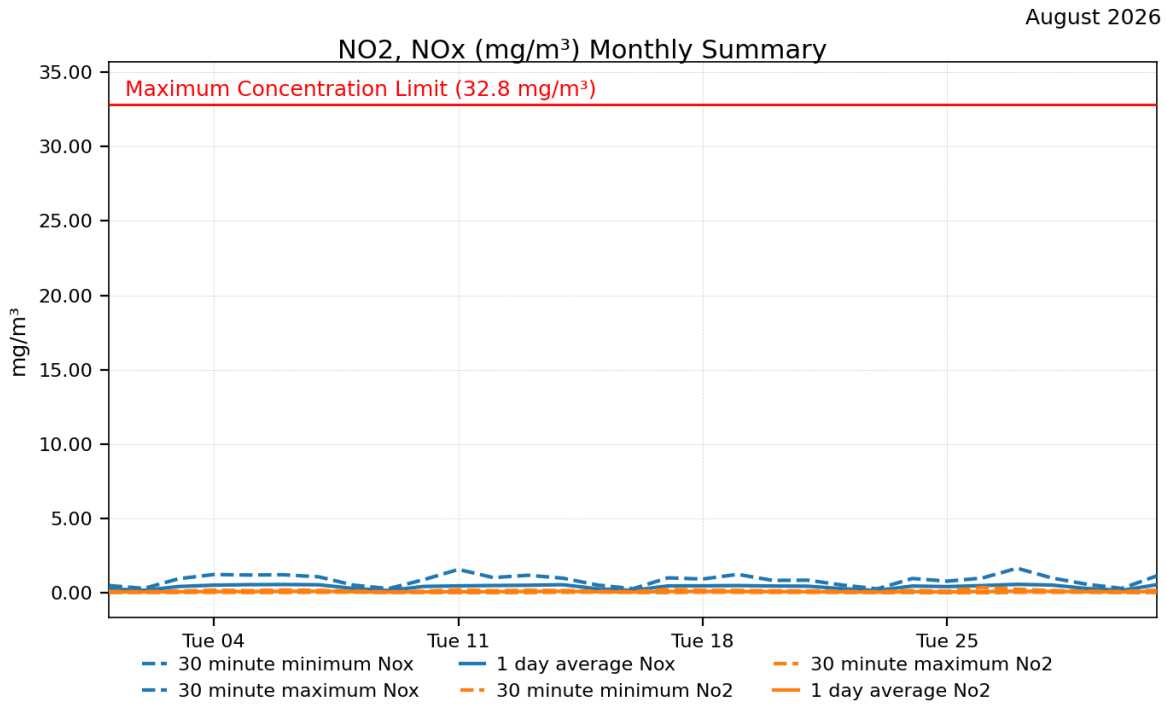


Figure 8. Sirius Rd NOx, NO_2 Averages

9.3.2.4 Sirius Rd Monthly PM_{10} Averages

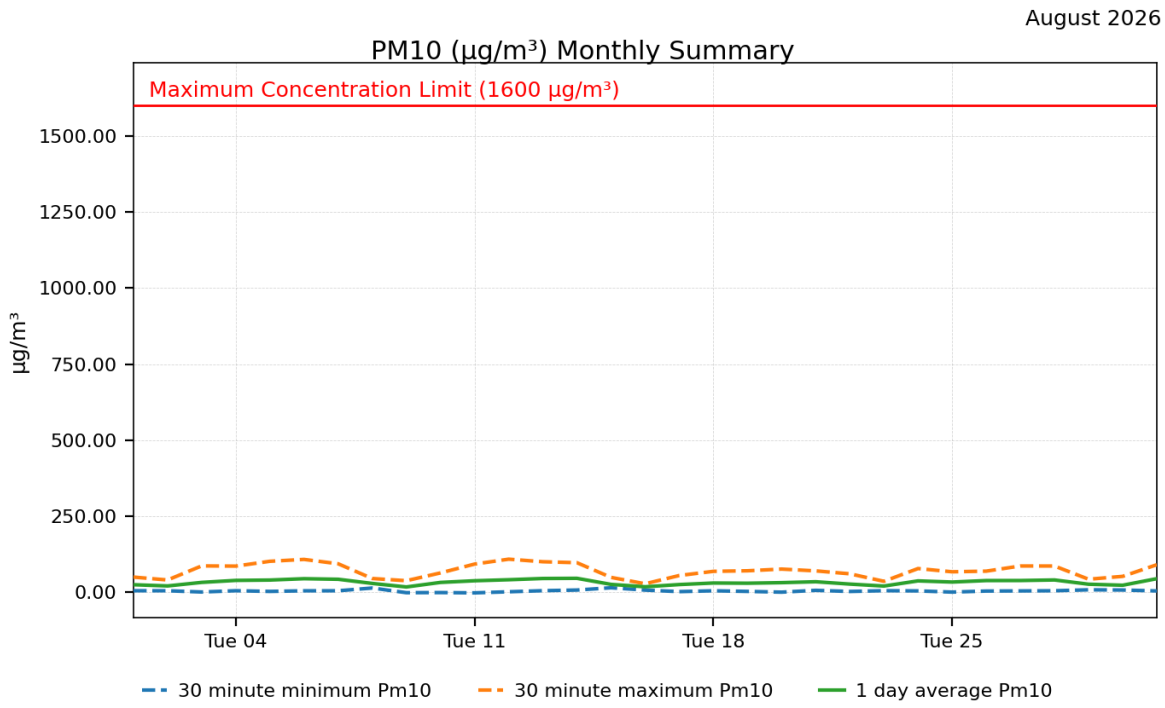


Figure 9. Sirius Rd PM_{10} Averages

9.3.3 Accumulative Loads

The following charts present annual accumulative total loads CO, NO_x, PM_{10} and VOC for the Lane Cove Tunnel ventilation stacks

9.3.3.1 Combined Stacks CO Accumulative Load

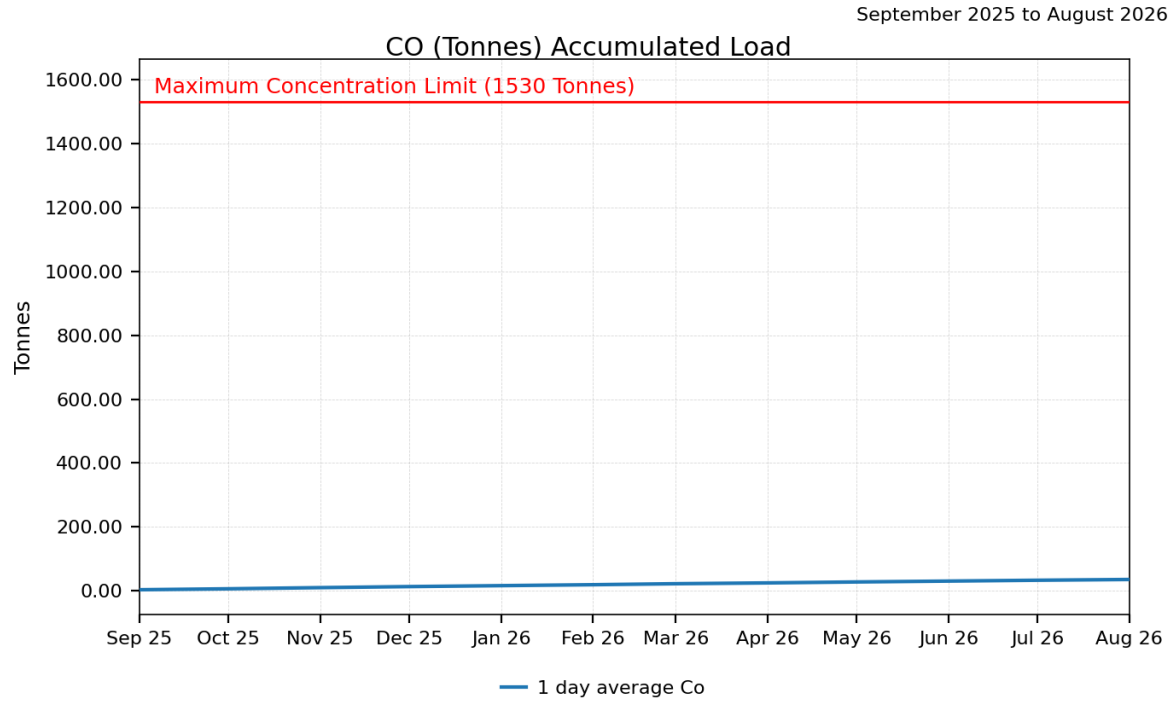


Figure 10. Combined Stacks CO Accumulative Load

9.3.3.2 Combined Stacks VOC Accumulative Load

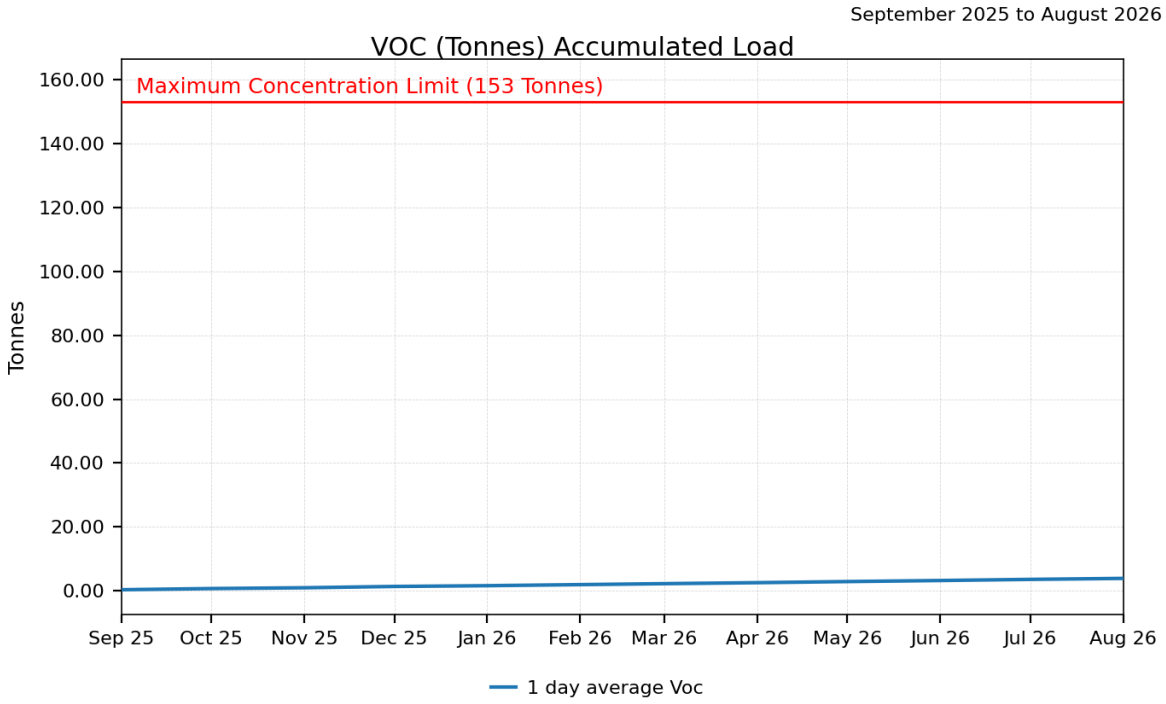


Figure 11. Combined Stacks VOC Accumulative Load

9.3.3.3 Combined Stacks NO_x Accumulative Load

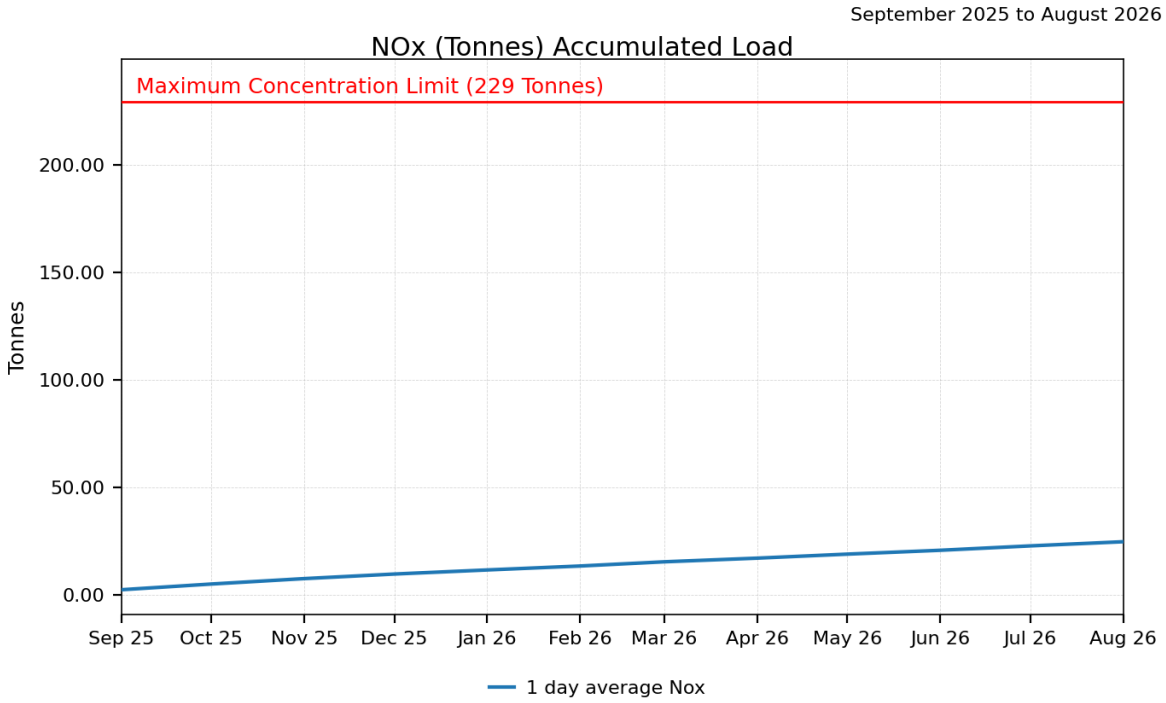


Figure 12. Combined Stacks NO_x Accumulative Load

9.3.3.4 Combined Stacks PM_{10} Accumulative Load

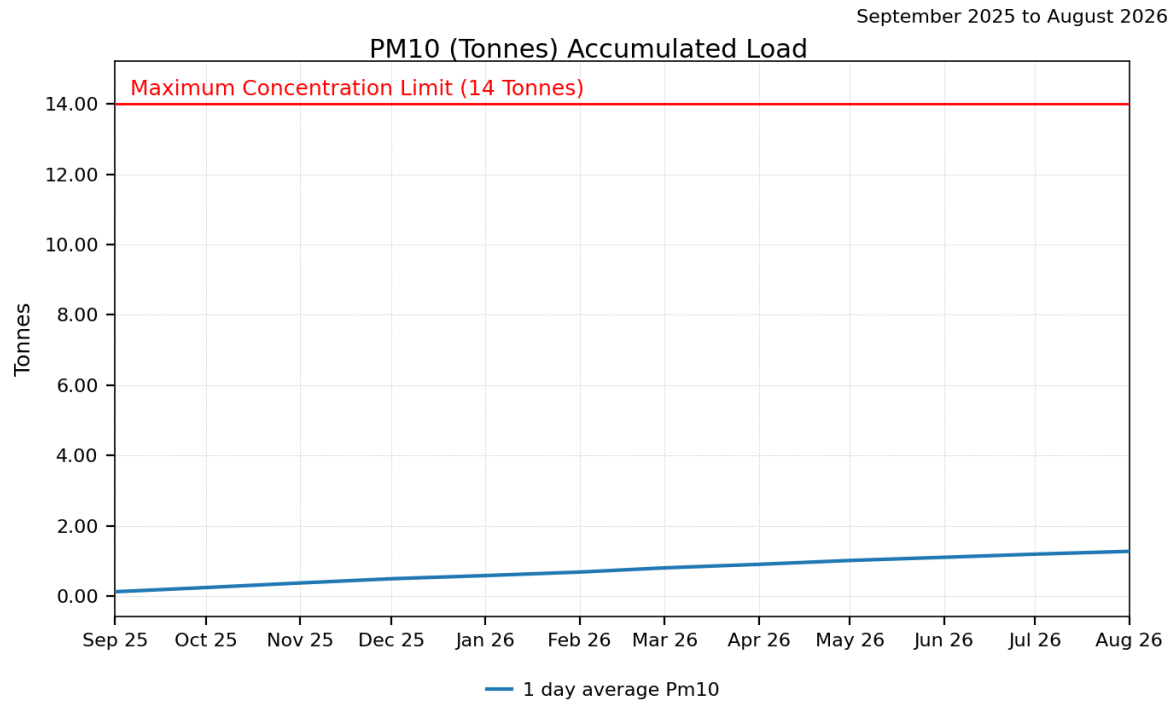


Figure 13. Combined Stacks NO_x Accumulative Load

9.3.4 Marden St Stack - Three Monthly Trends

The following charts present 1day average CO, NOx, PM10 and VOC for the Marden St Stack in three months.

The daily average is calculated from 30-minute average data.

9.3.4.1 Marden St Three Monthly CO 1day Averages

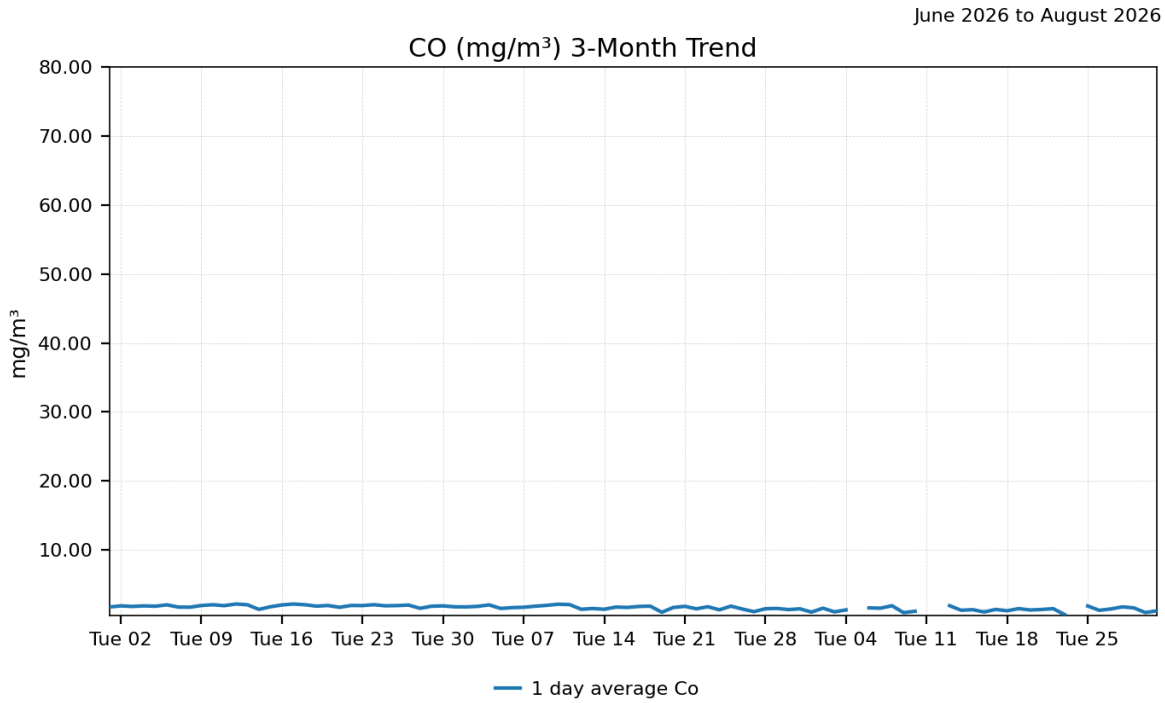


Figure 14. Marden St Three Monthly CO 1day Averages

9.3.4.2 Marden St Three Monthly VOC 1day Averages

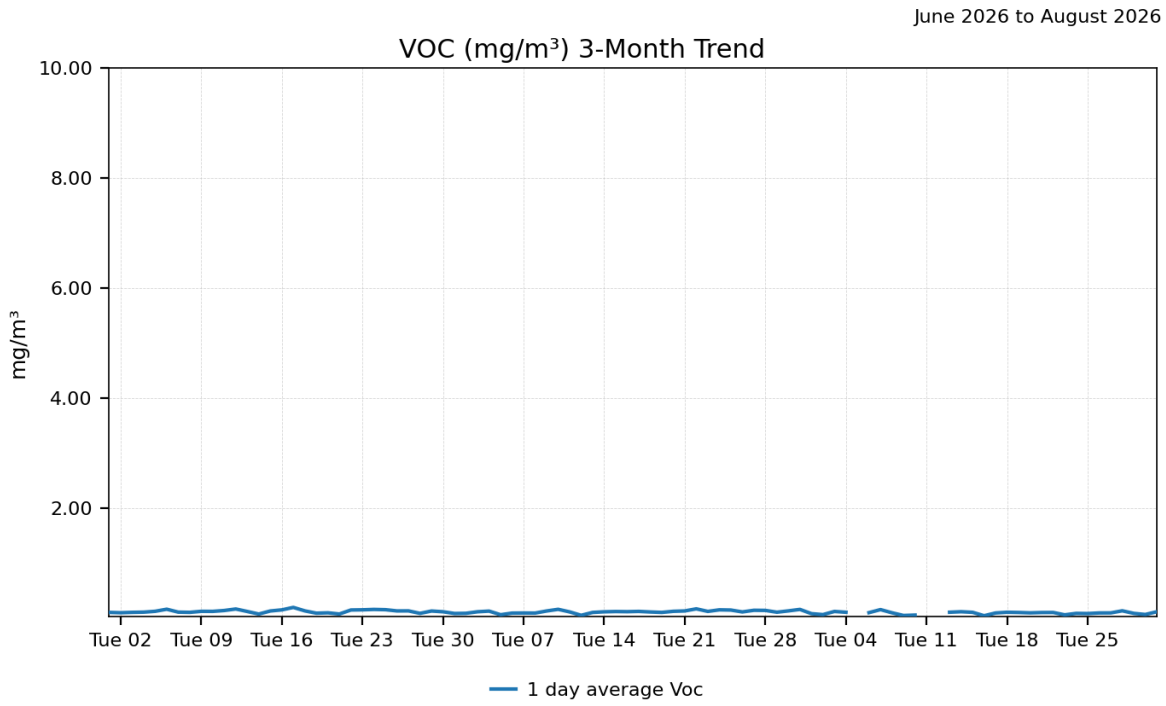


Figure 15. Marden St Three Monthly VOC 1day Averages

9.3.4.3 Marden St Three Monthly NO_x, NO_2 1day Averages

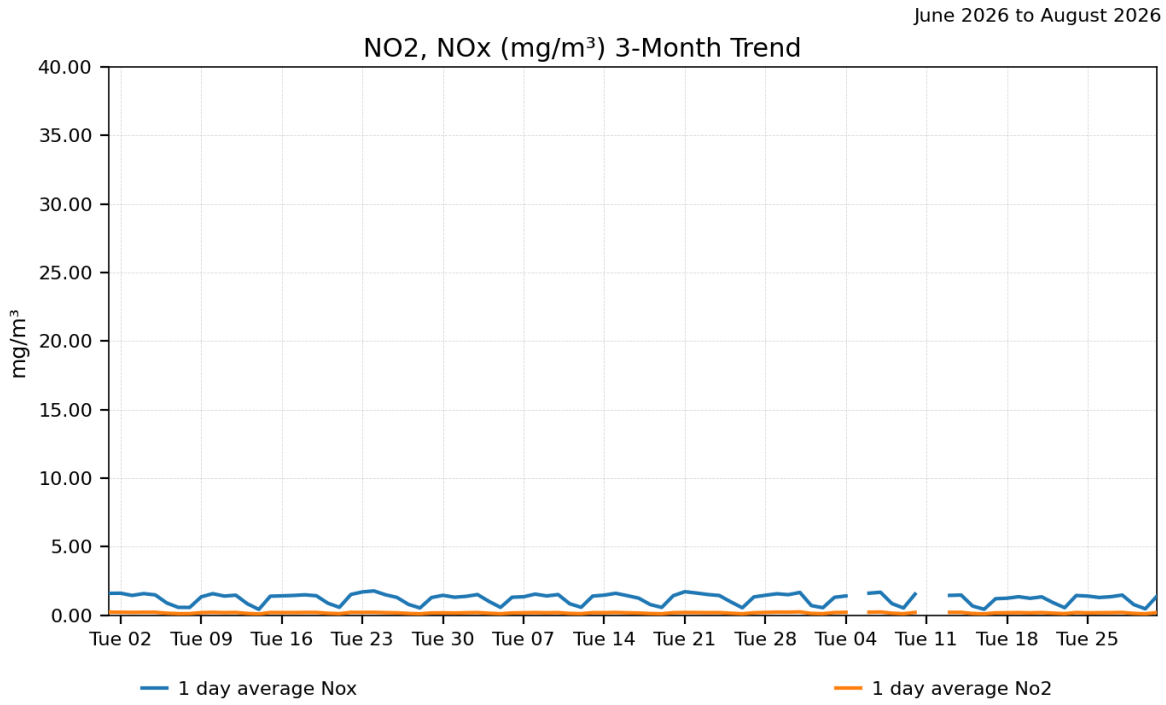


Figure 16. Marden St Three Monthly NO_x, NO_2 1day Averages

9.3.4.4 Marden St Three Monthly PM_{10} 1day Averages

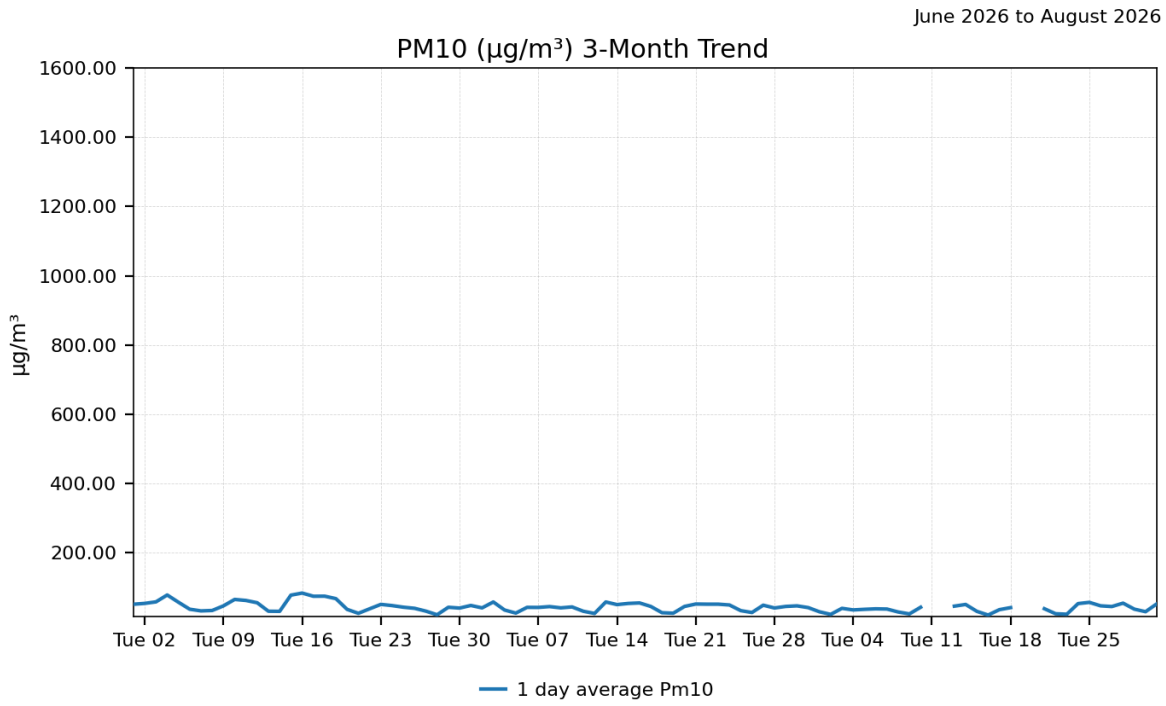


Figure 17. Marden St Three Monthly PM_{10} 1day Averages

9.3.5 Sirius Rd Stack - Three Monthly Trends

The following charts present 1-day average CO, NOx, PM10 and VOC for the Sirius Rd Stack in three months.

The daily average is calculated from 30-minute average data.

9.3.5.1 Sirius Rd Three Monthly CO 1day Averages

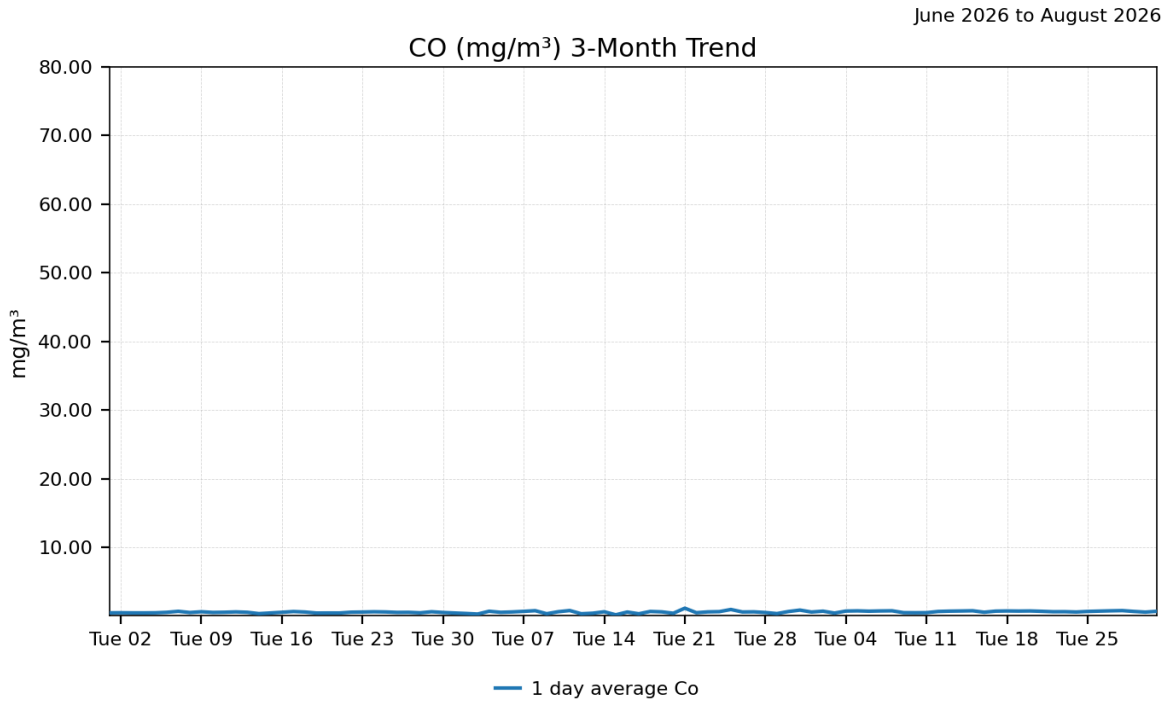


Figure 18. Sirius Rd Three Monthly CO 1day Averages

9.3.5.2 Sirius Rd Three Monthly VOC 1day Averages

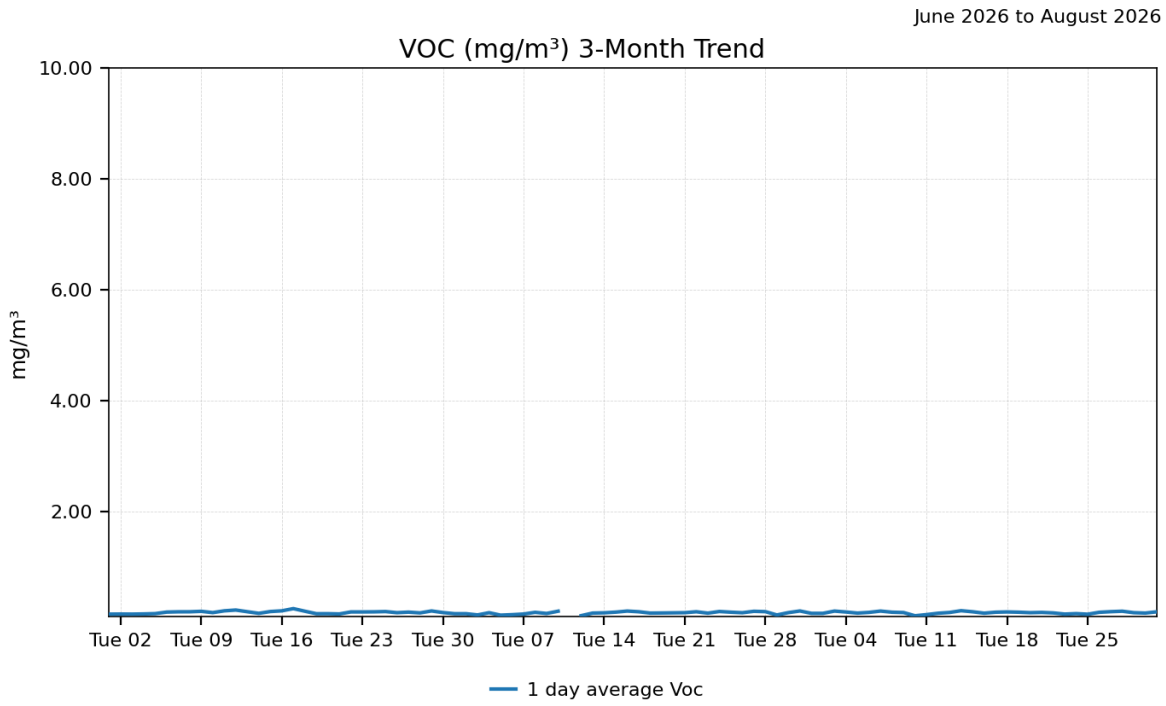


Figure 19. Sirius Rd Three Monthly VOC 1day Averages

9.3.5.3 Sirius Rd Three Monthly NO_x, NO_2 1day Averages

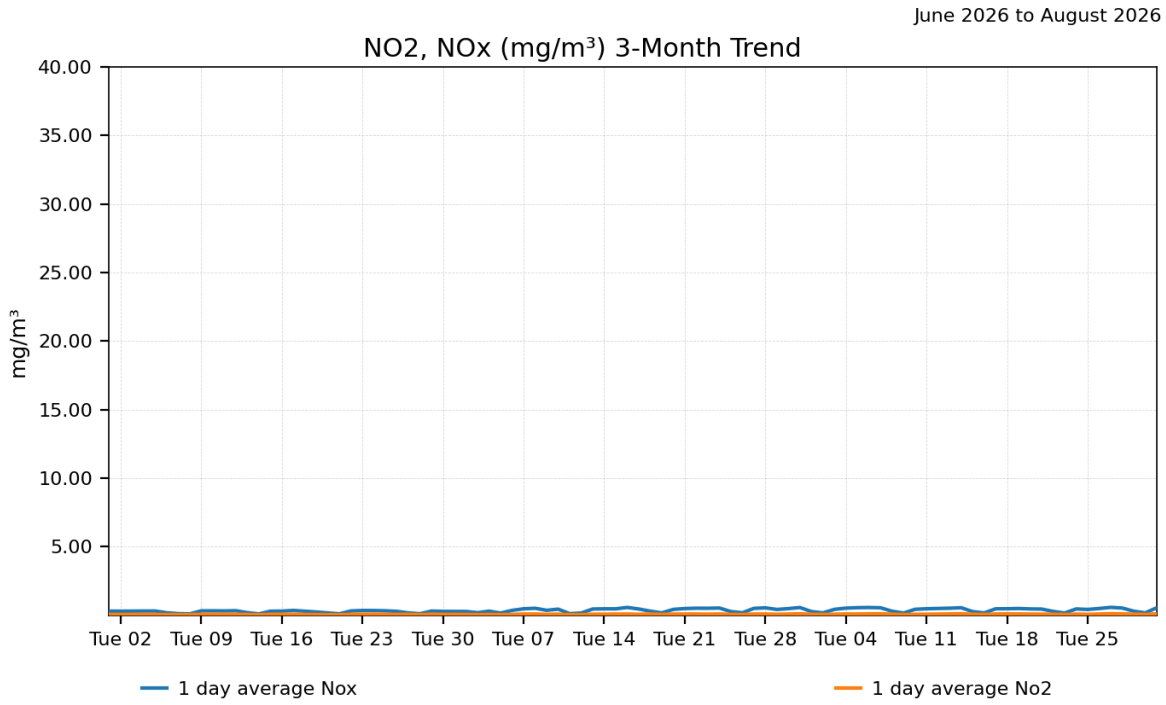


Figure 20. Sirius Rd Three Monthly NO_x, NO_2 1day Averages

9.3.5.4 Sirius Rd Three Monthly PM_{10} 1day Averages

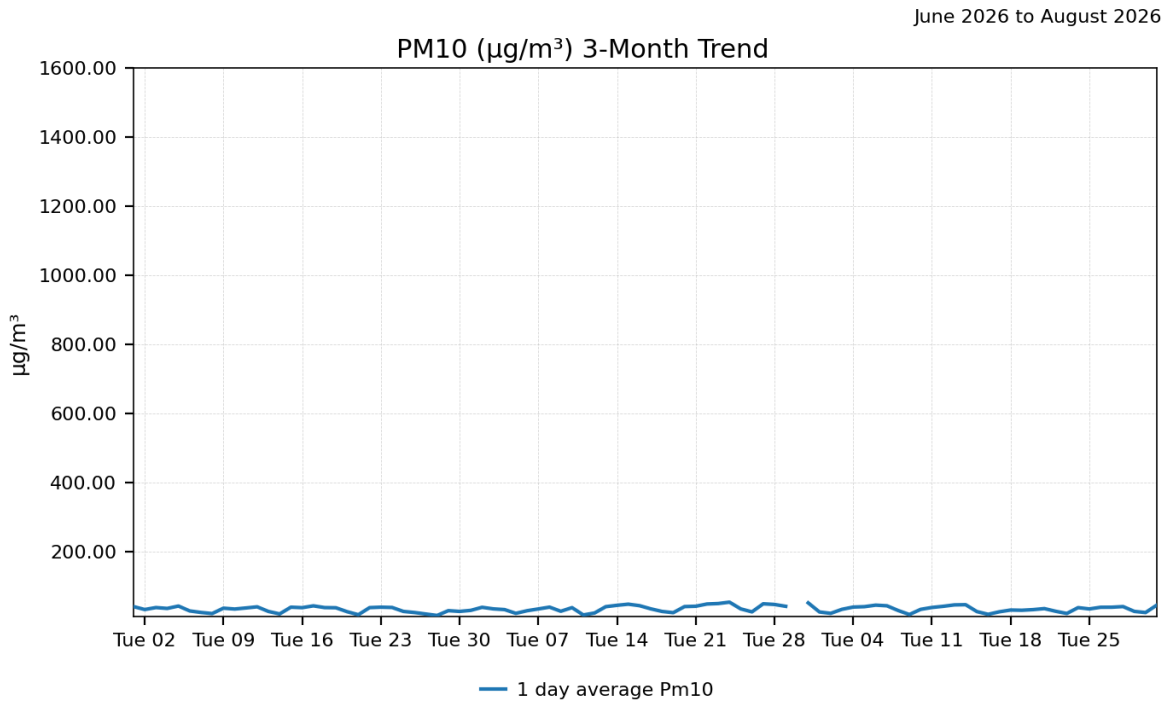


Figure 21. Sirius Rd Three Monthly PM_{10} 1day Averages

10. Data Exceptions

This section outlines any issues noted with the monitoring equipment during the reporting period.

Lane Cove Tunnel – Marden St Data Validation Table – August 2026						
Date from	**Date to**	**Parameters affected**	**Reason**	**Hours Affected**	**Validated By**	**Date**
1/08/2026 0:00	31/08/2026 23:55	NMHC	Offset applied to data: Offset A: -0.2 Offset B: -0.2	743.92	TA	10/09/2026
1/08/2026 0:00	31/08/2026 23:55	CO	Offset applied to data: Offset A: +0.3 Offset B: +0.3	743.92	TA	10/09/2026
1/08/2026 2:00	26/08/2026 2:25	PM10, PM2.5	Infrequent intermittent unrealistic data - negative	N/A	TA	10/09/2026
1/08/2026 19:05	1/08/2026 19:05	CO, NO, NO2, NOx, VOC	Missing data	0.0	TA	10/09/2026
4/08/2026 0:00	4/08/2026 0:05	All parameters	Missing data	0.08	TA	10/09/2026
5/08/2026 10:20	5/08/2026 14:50	All parameters	Maintenance	4.50	TA	10/09/2026
6/08/2026 11:35	6/08/2026 14:35	All parameters	Maintenance	3.00	TA	10/09/2026
11/08/2026 10:25	11/08/2026 16:00	All parameters	Maintenance	5.58	TA	10/09/2026
11/08/2026 16:05	11/08/2026 18:15	Stack Temp, Stack RH	Maintenance	2.17	TA	10/09/2026
11/08/2026 16:05	12/08/2026 10:55	PM10, PM2.5	Maintenance	18.83	TA	10/09/2026
12/08/2026 11:00	12/08/2026 17:50	All parameters	Maintenance	6.83	TA	10/09/2026
12/08/2026 18:25	12/08/2026 23:45	CO	Intermittent instrument reference adjustments	N/A	TA	10/09/2026
20/08/2026 10:50	20/08/2026 14:45	All parameters	Maintenance	3.92	TA	10/09/2026
23/08/2026 2:15	31/08/2026 23:55	CO	Multiplier applied to data: Multiplier A: 0.931532 Multiplier B: 0.931532	N/A	TA	10/09/2026
23/08/2026 22:50	25/08/2026 0:55	CO	Instrument fault	26.08	TA	10/09/2026

Table 19. Marden St Data Validation Table

Lane Cove Tunnel – Sirius Rd South Data Validation Table – August 2026						
Date from	**Date to**	**Parameters affected**	**Reason**	**Hours Affected**	**Validated By**	**Date**
1/08/2026 0:00	31/08/2026 23:55	NMHC	Offset applied to data: Offset A: -0.2 Offset B: -0.2	N/A	TA	10/09/2026
1/08/2026 0:00	2/08/2026 16:05	NO, NO2, NOx	Intermittent instrument faults	N/A	TA	10/09/2026
1/08/2026 7:20	1/08/2026 7:20	All parameters	Missing data	0.0	TA	10/09/2026
2/08/2026 12:20	28/08/2026 12:30	PM10, PM2.5	Infrequent intermittent unrealistic data - negative	N/A	TA	10/09/2026
3/08/2026 10:20	3/08/2026 15:30	All parameters	Maintenance	5.2	TA	10/09/2026
4/08/2026 11:45	4/08/2026 14:50	All parameters	Missing data	3.1	TA	10/09/2026
5/08/2026 14:10	5/08/2026 15:05	All parameters	Maintenance	0.9	TA	10/09/2026
11/08/2026 11:30	11/08/2026 13:50	All parameters	Maintenance	2.3	TA	10/09/2026
15/08/2026 19:10	17/08/2026 11:10	NO, NO2, NOx	Intermittent instrument faults	N/A	TA	10/09/2026
17/08/2026 11:15	17/08/2026 13:40	All parameters	Maintenance	2.4	TA	10/09/2026

Table 20. Sirius Rd South Data Validation Table

Lane Cove Tunnel – Sirius Rd North Data Validation Table – August 2026						
Date from	**Date to**	**Parameters affected**	**Reason**	**Hours Affected**	**Validated By**	**Date**
1/08/2026 0:05	3/08/2026 15:05	NMHC	Multiplier applied to data: Multiplier A: 0.950617 Multiplier B: 0.950617	N/A	TA	10/09/2026
1/08/2026 0:05	3/08/2026 15:05	CH4	Multiplier applied to data: Multiplier A: 0.936364 Multiplier B: 0.936364	N/A	TA	10/09/2026
1/08/2026 2:05	3/08/2026 15:05	NO, NO2, NOx	Multiplier applied to data: Multiplier A: 1.122016 Multiplier B: 1.122016	N/A	TA	10/09/2026
4/08/2026 3:05	30/08/2026 9:55	PM10, PM2.5	Infrequent intermittent unrealistic data - negative	N/A	TA	10/09/2026
3/08/2026 10:25	3/08/2026 16:00	All parameters	Maintenance	5.6	TA	10/09/2026
3/08/2026 16:05	3/08/2026 23:40	CH4	Instrument stabilisation following maintenance	7.6	TA	10/09/2026
3/08/2026 16:05	1/09/2026 0:00	NO, NO2, NOx	Multiplier applied to data: Multiplier A: 1.014388 Multiplier B: 1.084615	N/A	TA	10/09/2026
5/08/2026 13:45	5/08/2026 14:00	All parameters	Maintenance	0.3	TA	10/09/2026
12/08/2026 2:05	31/08/2026 23:55	NMHC	Multiplier applied to data: Multiplier A: 0.953094 Multiplier B: 0.953094	N/A	TA	10/09/2026
12/08/2026 2:05	31/08/2026 23:55	CH4	Multiplier applied to data: Multiplier A: 0.931683 Multiplier B: 0.931683	N/A	TA	10/09/2026

Table 21. Sirius Rd North Data Validation Table

11. Report Summary

There was nil above goal readings recorded during the reporting period.

12. Data validation explanations

Automatic background check refers to when analyser samples zero air and measures the level of the concentration voltage. This voltage is taken as the zero signal level and this value is subtracted from any subsequent readings as an active zero compensation. This is the analyser's fine zero measurement.

Calibration check outside tolerance refers to when the calibration values are outside the tolerance limits set for the precision check.

Offset or Multiplier Applied to data refers to an offset or multiplier applied to the data. This operation may be performed for a number of reasons including: (a) when a clear trend / drift outside the tolerance limit can be demonstrated by repeated operation precision checks, (b) when a correction is required on previously logged data due to a calibration check being outside the allowable tolerance

Data transmission error refers to a period of time when the instrument could not transmit data. This may be due to a communication fault between the logger and the instrument.

Equipment malfunction/instrument fault refers to a period of time when the instrument was not in the normal operating mode and did not measure a representative value of the existing conditions.

Missing data/data not available refers to a period of time when either data has been lost or could not be collected.

Instrument Alarm refers to an alarm produced by the instrument. A range of alarms can be produced depending on how the operation of the instrument is being affected.
Instrument out of service refers to an unavailability of data due to an instrument being shut down for repair, maintenance, or factory calibration.

Logger error refers to when an error occurs and instrument readings are not correctly recorded by the logger.

Maintenance refers to a period of time when the logger / instrument was unavailable due to maintenance.

Overnight span/zero out of tolerance refers to when the span/zero reading measured by the analyser during an automatic precision check falls outside of the expected concentration limits.

Power Interruption refers to no power to the station therefore no data was collected at this time.

Remote Calibration refers to when a technician remotely connects to the station and manually performs a span check.

Warm up after power interruption refers to the start up period of an instrument after power has been restored.
